


JJC BIO-FILTRATION PROJECT

ID	Task Name	Duration	Start	Finish	Oct 18, '09							Oct 25, '09							Nov 1, '09					
					W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M
1	Pre-Construction Meeting	1 day	Thu 10/15/09	Thu 10/15/09																				
2	Coordinate to work around Lake Dredger	1 day	Mon 10/19/09	Mon 10/19/09																				
3	Mobilize	1 day	Tue 10/20/09	Tue 10/20/09																				
4	Start Date	0 days	Tue 10/20/09	Tue 10/20/09																				
5	Stake Silt Fence	0.5 days	Tue 10/20/09	Tue 10/20/09																				
6	Install Construction Entrances	0.5 days	Wed 10/21/09	Wed 10/21/09																				
7	Install Silt Fence	1 day	Wed 10/21/09	Wed 10/21/09																				
8	Stake Bio-Swale & Wetland Cell	2 days	Tue 10/20/09	Wed 10/21/09																				
9	Stake Rock Check Dams	0.5 days	Wed 10/21/09	Wed 10/21/09																				
10	Excavate Bio-Swale & Wet Cell	7 days	Wed 10/21/09	Mon 11/2/09																				
11	Install Rip Rap in Bio-Swale and Wet Cell	3 days	Tue 10/27/09	Fri 10/30/09																				
12	Culvert-remove and replace	2 days	Wed 10/28/09	Thu 10/29/09																				
13	Install Rock Check Dams	2 days	Mon 11/2/09	Tue 11/3/09																				
14	Treat Invasive in Exist. Trench	1 day	Tue 10/27/09	Tue 10/27/09																				
15	Landscape Bio-Swale & Wet Cell	5 days	Mon 10/26/09	Mon 11/2/09																				
16	Install Trees and Shrubs	1 day	Tue 11/3/09	Tue 11/3/09																				
17	Final Clean Up	0.5 days	Tue 11/3/09	Tue 11/3/09																				

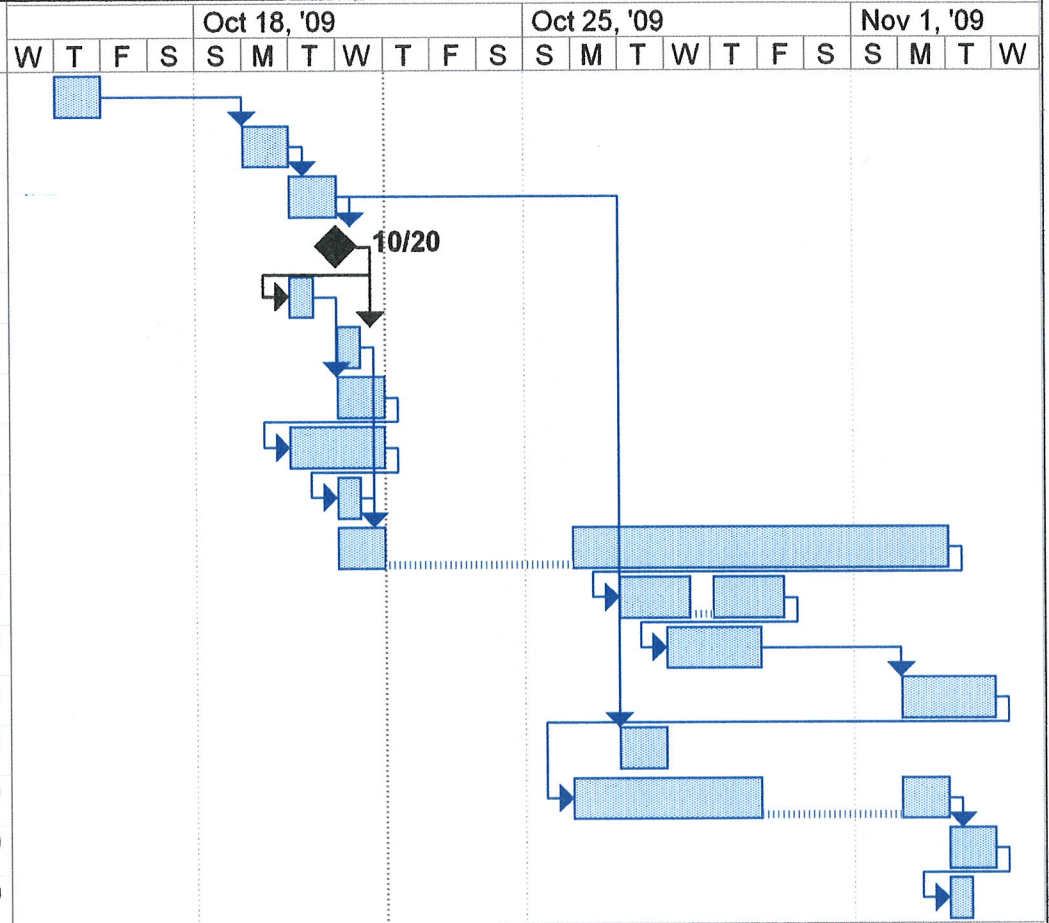

JJC Bio Filtration Project 1st Updated Schedule 10-22-09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
